

ID	Task Name	Duration	Start	Finish	3rd Quarter			1st Quarter			3rd Quarter	
					J	S	N	J	M	M	J	
1	Emrex	785 days?	Thu 1.1.15	Tue 2.1.18								
2	WP1:Project mgmt and quality assurance	783 days	Thu 1.1.15	Sun 31.12.17								
3	Project mgmt	783 days?	Thu 1.1.15	Sun 31.12.17								
4	Risk plan	23 days	Mon 2.3.15	Wed 1.4.15								
5	Stakeholder Forum workshop 1	1 day	Wed 21.10.15	Wed 21.10.15								
6	Stakeholder Forum workshop 2	1 day	Mon 16.5.16	Mon 16.5.16								
7	1st year report	0 days	Mon 1.2.16	Mon 1.2.16								
8	2nd year report	0 days	Tue 31.1.17	Tue 31.1.17								
9	Final report	23 days	Thu 30.11.17	Sun 31.12.17								
10	Quality Assurance	783 days?	Thu 1.1.15	Sun 31.12.17								
11	Quality plan	30 days	Thu 19.2.15	Wed 1.4.15								
12	1st quality evaluation	0 days	Mon 1.2.16	Mon 1.2.16								
13	2nd quality evaluation	0 days	Tue 31.1.17	Tue 31.1.17								
14	Final quality report	0 days	Thu 30.11.17	Thu 30.11.17								
15	Planning hand-over	261 days?	Mon 2.1.17	Sun 31.12.17								
16	WP2: Planning	239 days?	Thu 1.1.15	Tue 1.12.15								
17	Trial and testing planning	152 days?	Thu 1.1.15	Fri 31.7.15								
18	Decision on HEIS to include in pilot	0 days	Mon 1.6.15	Mon 1.6.15								
19	Trial planning ready for WP4	0 days	Tue 30.6.15	Tue 30.6.15								

Project: Emrex_projectplan_v6
Date: Fri 27.2.15

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

ID	Task Name	Duration	Start	Finish	3rd Quarter			1st Quarter			3rd Quarter	
					J	S	N	J	M	M	J	
20	Requirements, use cases	45 days?	Thu 1.1.15	Wed 4.3.15								
21	Planning workshop	0 days	Wed 28.1.15	Wed 28.1.15								
22	Final planning workshop	0 days	Mon 27.4.15	Mon 27.4.15								
23	Overall technical solution agreed	0 days	Thu 19.2.15	Thu 19.2.15								
24	Uses cases ready	0 days	Wed 1.4.15	Wed 1.4.15								
25	National Contact point specifications	68 days?	Thu 29.1.15	Mon 4.5.15								
26	Student Mobile plug-in specifications	68 days?	Thu 29.1.15	Mon 4.5.15								
27	HW,SW, licences specifications	68 days?	Thu 29.1.15	Mon 4.5.15								
28	Specifications ready for development and subcontractors	0 days	Mon 4.5.15	Mon 4.5.15								
29	Legal conditions for using Emrex	239 days?	Thu 1.1.15	Tue 1.12.15								
30	WP3: IT development	434 days?	Tue 5.5.15	Fri 30.12.16								
31	Start up meeting	0 days	Fri 15.5.15	Fri 15.5.15								
32	Preparing subcontracting	87 days?	Tue 5.5.15	Wed 2.9.15								
33	Security	2,25 mons	Mon 1.6.15	Fri 31.7.15								
34	Development of National Contact Points	4,35 mons	Mon 3.8.15	Tue 1.12.15								
35	First version of NCP ready for pilot	0 days	Tue 1.12.15	Tue 1.12.15								
36	Development of Student Mobility Plug-ins	2 wks	Mon 19.10.15	Fri 30.10.15								
37	First version of SMP ready	0 days	Fri 30.10.15	Fri 30.10.15								
38	Development of EMREG	87 days?	Mon 3.8.15	Tue 1.12.15								

Project: Emrex_projectplan_v6
Date: Fri 27.2.15

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

ID	Task Name	Duration	Start	Finish	3rd Quarter			1st Quarter			3rd Quarter	
					J	S	N	J	M	M	J	
39	EMREG ready	0 days	Tue 1.12.15	Tue 1.12.15								
40	Pilot / UAT	24 days?	Wed 2.12.15	Mon 4.1.16								
41	Final acceptance	0 days	Mon 4.1.16	Mon 4.1.16								
42	Deploying Student Mobilities Plug-ins	45 days?	Mon 29.2.16	Fri 29.4.16								
43	Field trial network ready	0 days	Fri 29.4.16	Fri 29.4.16								
44	Technical documentation	110 days?	Mon 3.8.15	Fri 1.1.16								
45	Change management and support during field trial	261 days?	Fri 1.1.16	Fri 30.12.16								
46	WP4: Trial - testing	370 days?	Mon 3.8.15	Mon 2.1.17								
47	Set-up of Field trial	109 days?	Mon 3.8.15	Thu 31.12.15								
48	Workshop on field trial	1 day	Tue 15.9.15	Tue 15.9.15								
49	Pilot testing	44 days?	Mon 2.11.15	Thu 31.12.15								
50	Running Field trial	261 days?	Fri 1.1.16	Fri 30.12.16								
51	Check-point after set-up in first countries	0 days	Mon 2.5.16	Mon 2.5.16								
52	Data collected from trial	0 days	Mon 2.1.17	Mon 2.1.17								
53	WP5: Evaluation	632 days?	Thu 1.1.15	Fri 2.6.17								
54	Prepare evaluation methodology and support trial setup	262 days?	Thu 1.1.15	Fri 1.1.16								
55	Evaluation	370 days?	Mon 4.1.16	Fri 2.6.17								
56	Final report	0 days	Fri 2.6.17	Fri 2.6.17								
57	WP6: Standardization	219 days?	Mon 2.3.15	Thu 31.12.15								

Project: Emrex_projectplan_v6 Date: Fri 27.2.15	Task		Inactive Milestone		Finish-only	
	Split		Inactive Summary		External Tasks	
	Milestone		Manual Task		External Milestone	
	Summary		Duration-only		Progress	
	Project Summary		Manual Summary Rollup		Deadline	
	External Tasks		Manual Summary			
	External Milestone		Start-only			


ID	Task Name	Duration	Start	Finish	3rd Quarter			1st Quarter			3rd Quarter		
					J	S	N	J	M	M	J	J	S
58	Identify possible areas for standardization	65 days?	Mon 2.3.15	Sun 31.5.15									
59	Report on existing standards	0 days	Mon 1.6.15	Mon 1.6.15									
60	Develop proposals for standardization	154 days?	Mon 1.6.15	Thu 31.12.15									
61	Glossary , models and examples	0 days	Wed 30.9.15	Wed 30.9.15									
62	Submit proposals	0 days	Tue 1.12.15	Tue 1.12.15									
63	Final report	0 days	Thu 31.12.15	Thu 31.12.15									
64	WP7: Dissemination and scaling-up	783 days?	Thu 1.1.15	Sun 31.12.17									
65	Plan dissemination activities	108 days?	Thu 1.1.15	Mon 1.6.15									
66	Basic material done	0 days	Wed 1.4.15	Wed 1.4.15									
67	Marketing plan	0 days	Fri 1.5.15	Fri 1.5.15									
68	External website launched	0 days	Wed 15.4.15	Wed 15.4.15									
69	Create dissemination material	415 days?	Mon 1.6.15	Fri 30.12.16									
70	Groningen Declaration	2 days	Tue 5.5.15	Wed 6.5.15									
71	EUNIS2015	2 days	Wed 10.6.15	Thu 11.6.15									
72	Conference in 2016	0 days	Wed 1.6.16	Wed 1.6.16									
73	Conference in 2017	0 days	Thu 1.6.17	Thu 1.6.17									
74	Active marketing of EMREX findings	261 days?	Mon 2.1.17	Sun 31.12.17									
75	Communciation plan for each country	0 days	Wed 30.9.15	Wed 30.9.15									
76	New steering group established	0 days	Wed 1.11.17	Wed 1.11.17									

Project: Emrex_projectplan_v6 Date: Fri 27.2.15	Task		Inactive Milestone		Finish-only	
	Split		Inactive Summary		External Tasks	
	Milestone		Manual Task		External Milestone	
	Summary		Duration-only		Progress	
	Project Summary		Manual Summary Rollup		Deadline	
	External Tasks		Manual Summary			
	External Milestone		Start-only			




Project: Emrex_projectplan_v6
Date: Fri 27.2.15

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

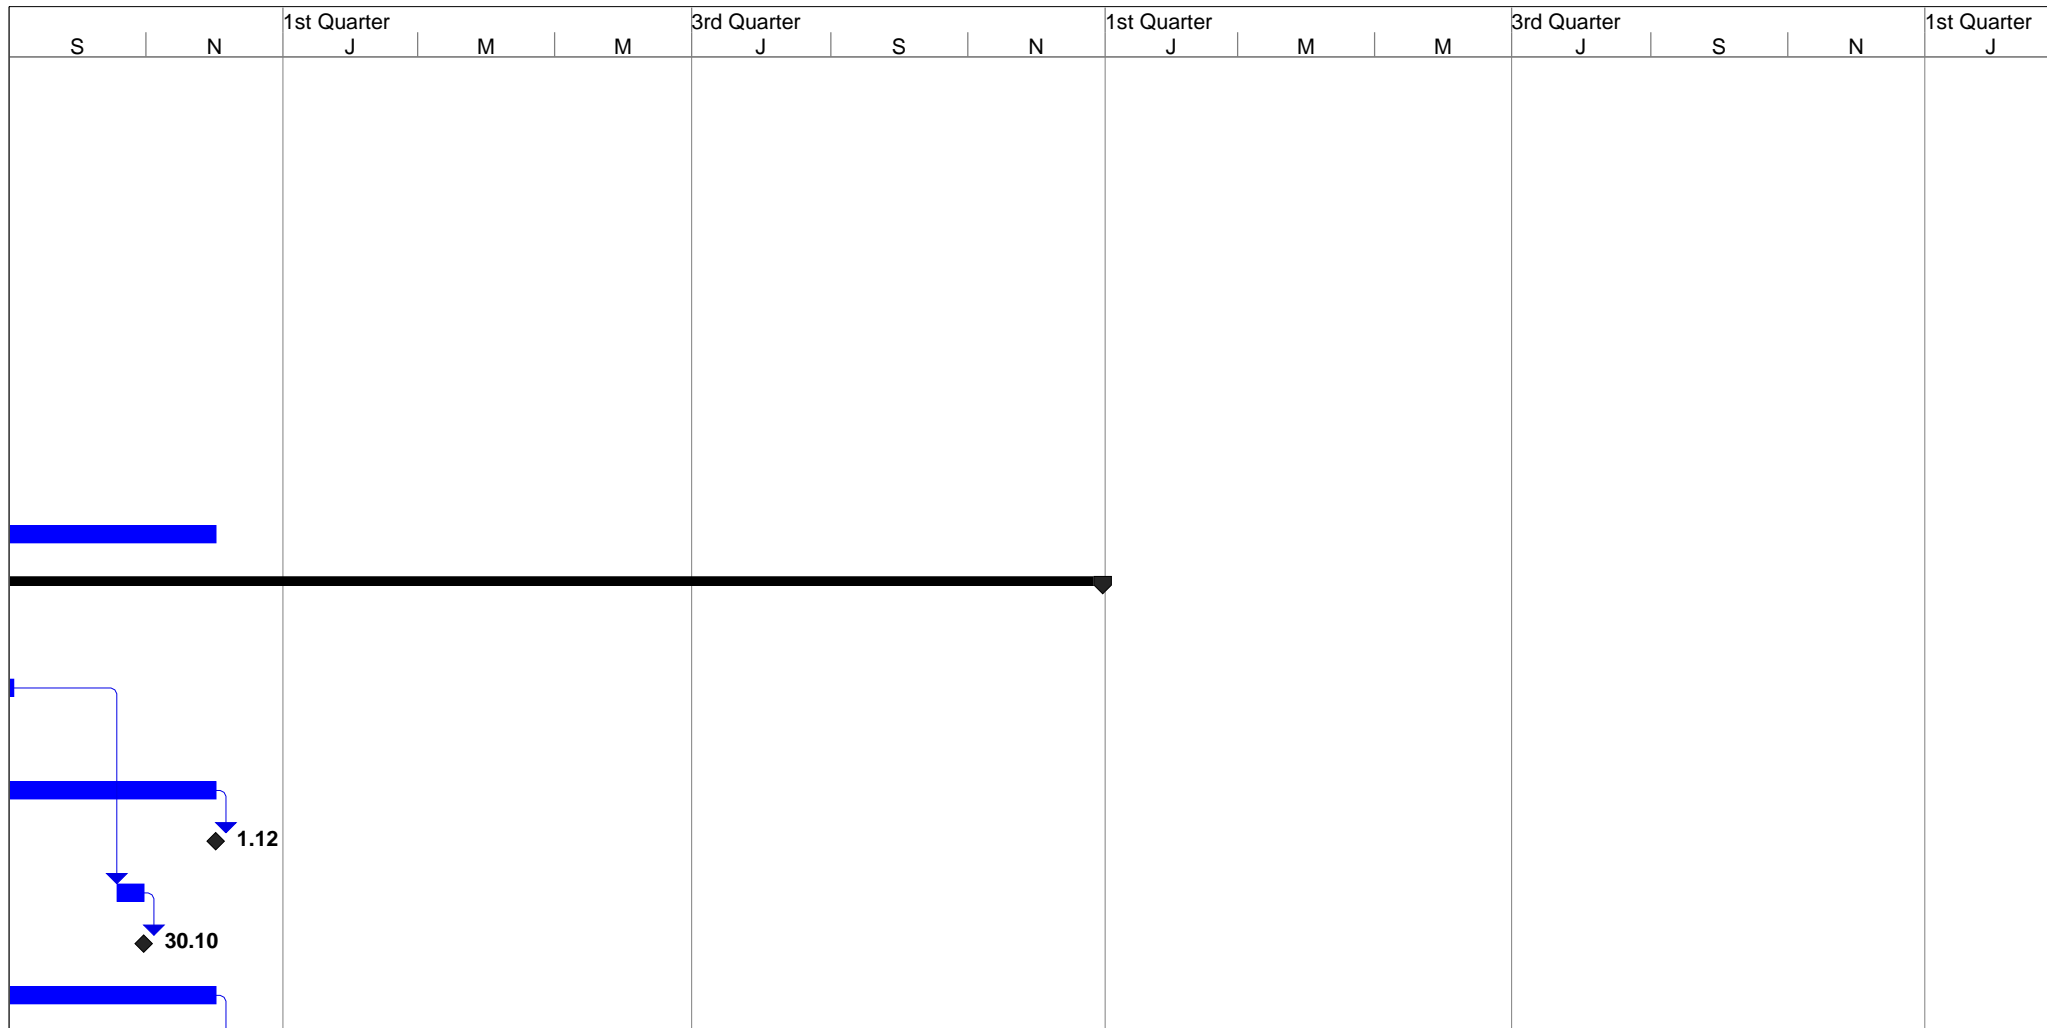


Project: Emrex_projectplan_v6
Date: Fri 27.2.15

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

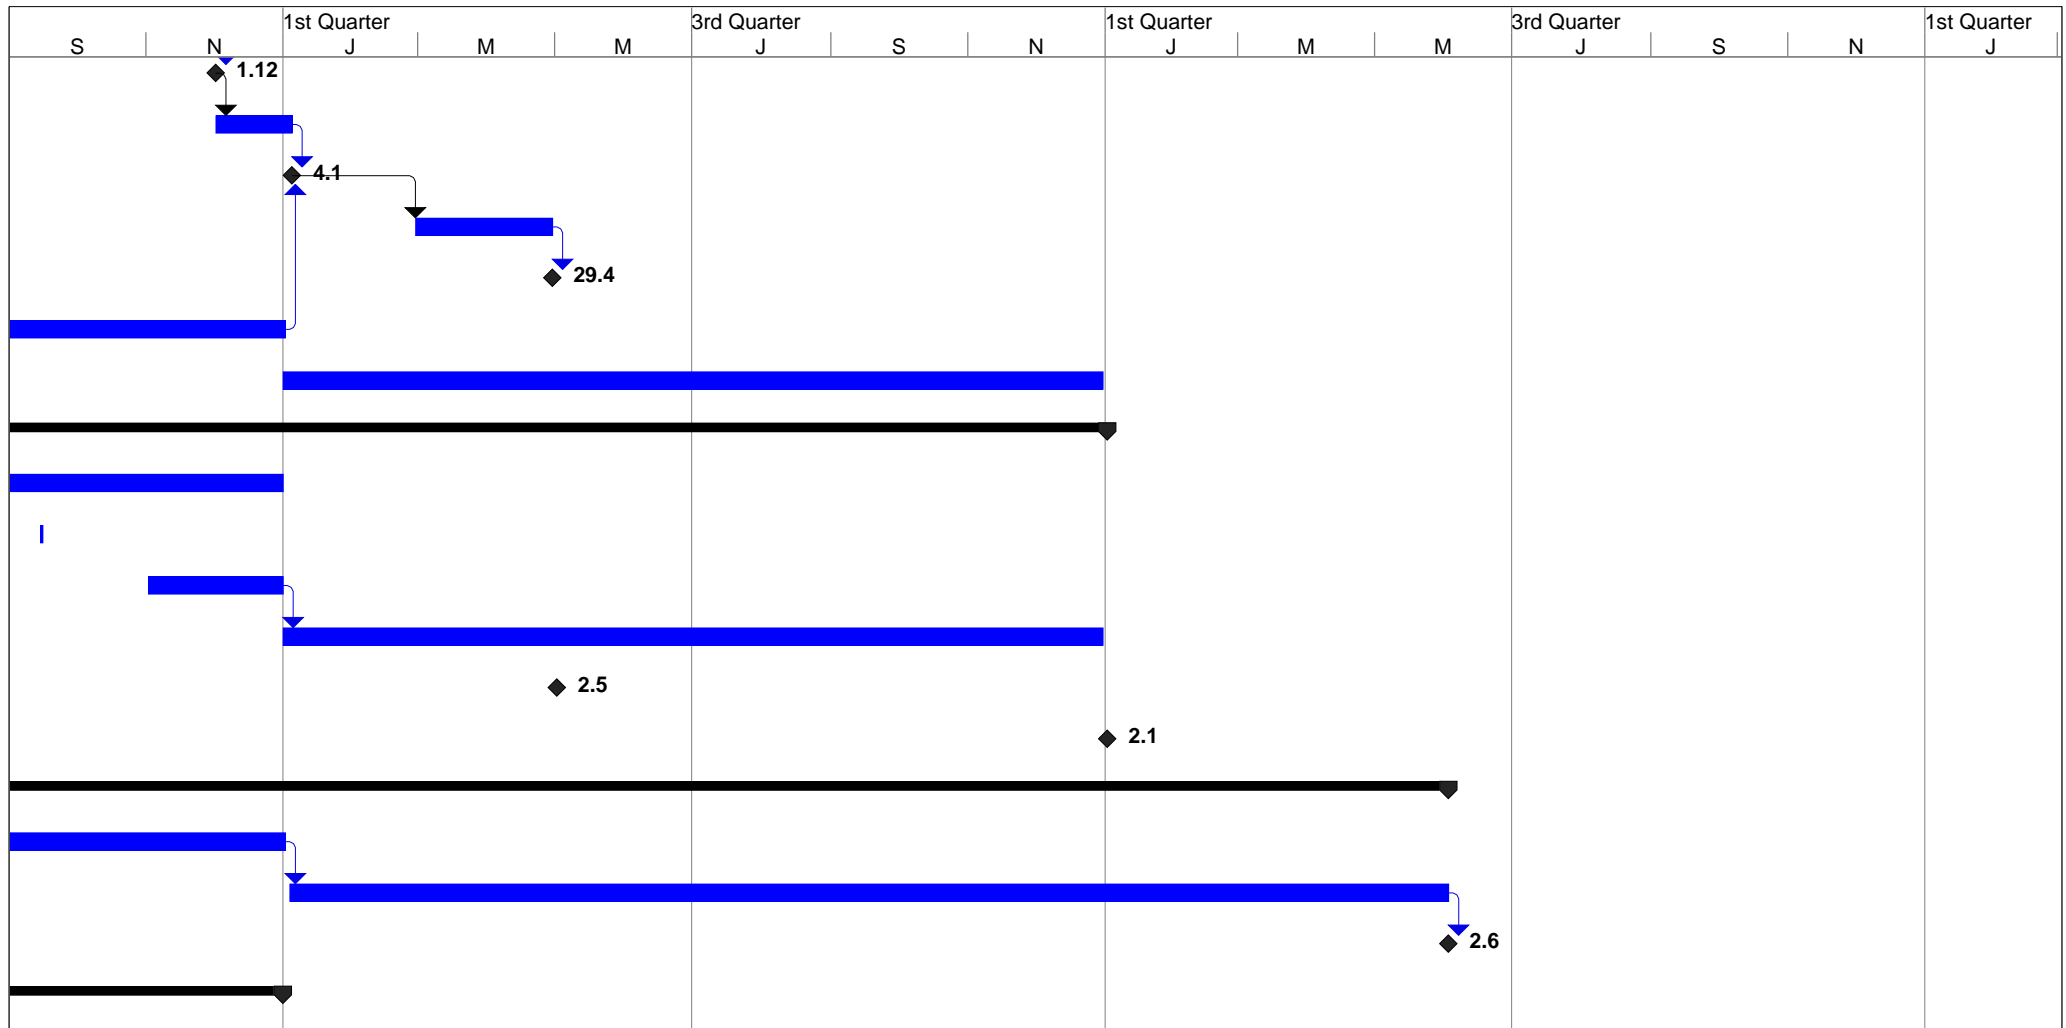

Project: Emrex_projectplan_v6
Date: Fri 27.2.15

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

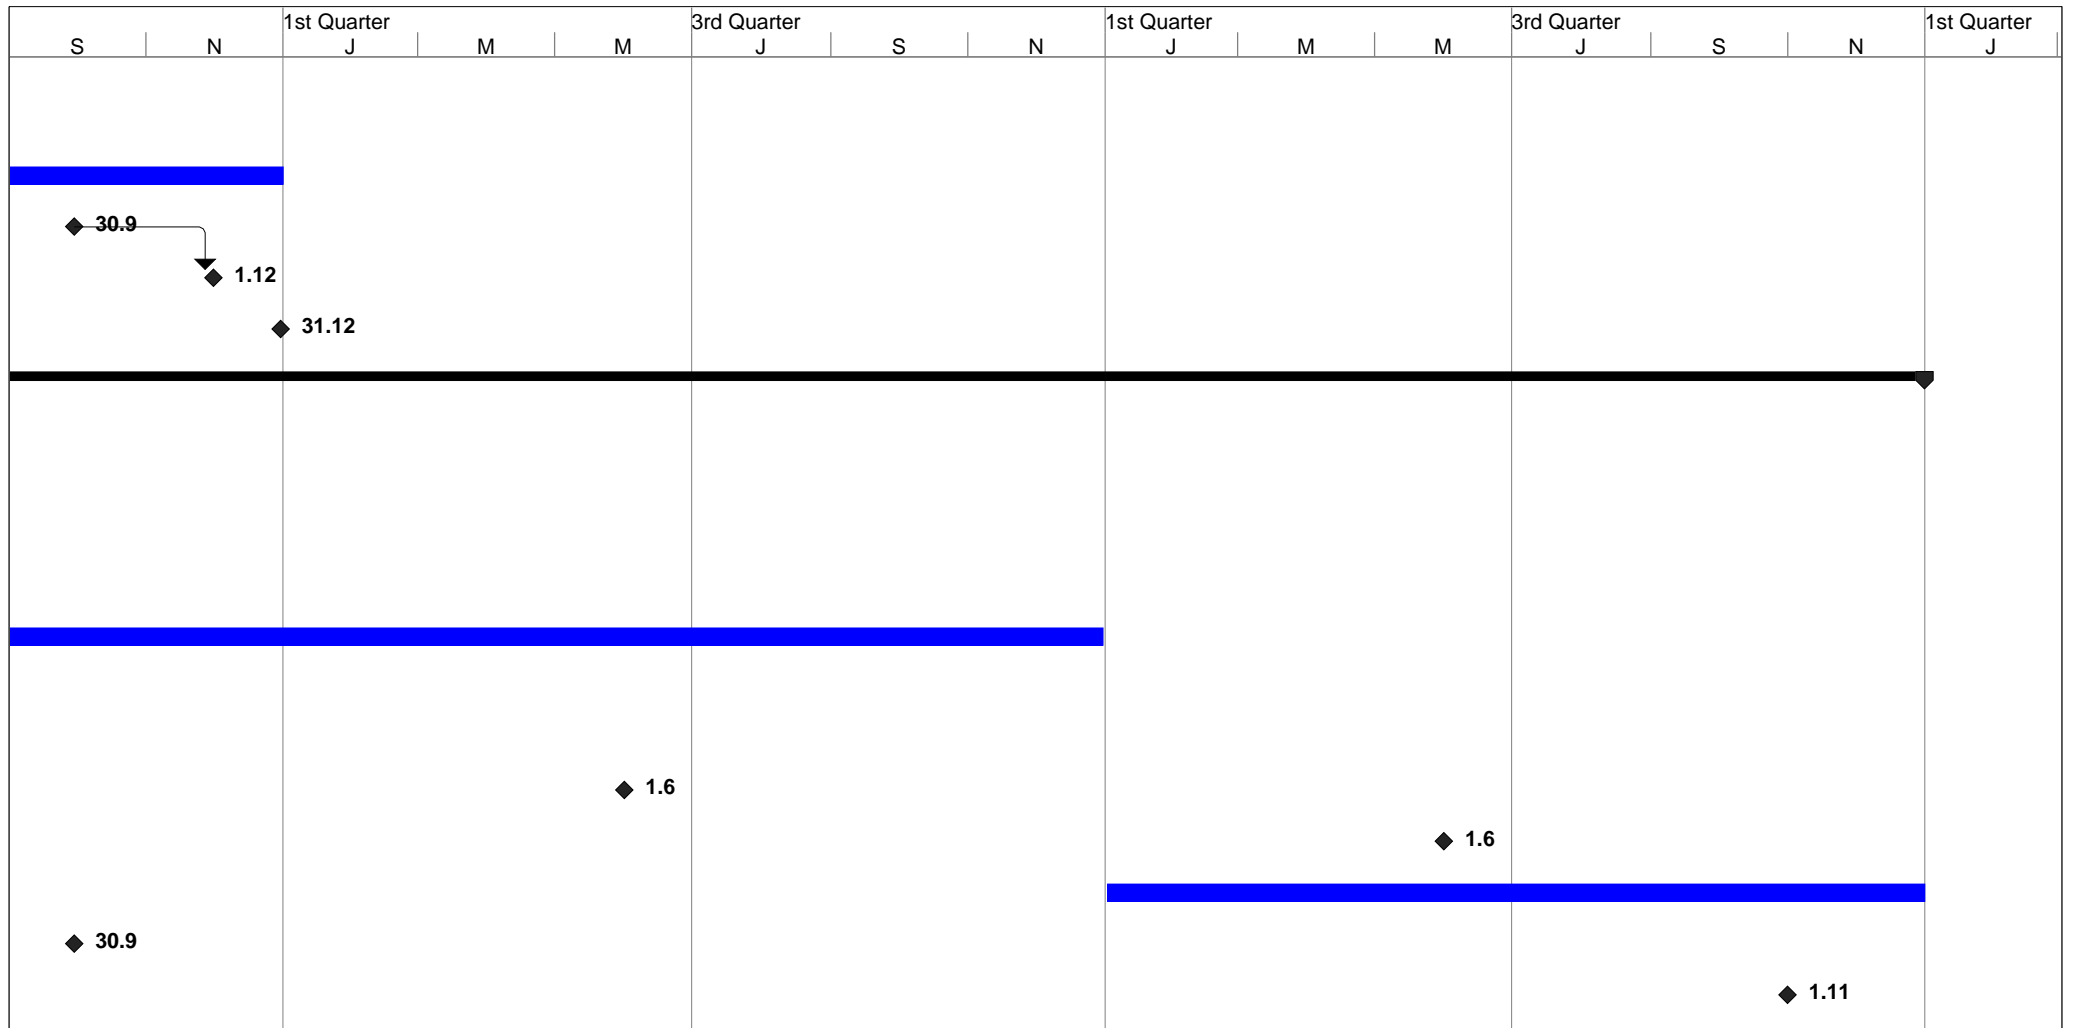

Project: Emrex_projectplan_v6
Date: Fri 27.2.15

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			
